

Des Plaines River Water Reclamation Facility Improvements Phase 2B, 3 Project

*Construction
Update*

February 3, 2016



- Contractor: Williams Brothers Construction Inc. ,
Peoria
- Contract amount: \$ 32 million
- Project currently 20% complete
- July 2017 Project completion

Water Reclamation Facility Site Map





Location of Biosolids Drying Building #60















Finishing the suspended slab over the truck receiving silo.



Forms for the foundation walls around the perimeter of the Dryer Building.



Location of Denitrification Tank





Construction of Denitrification Tank










Influent Junction Box #93
Rehab required a large bypass
pumping operation.







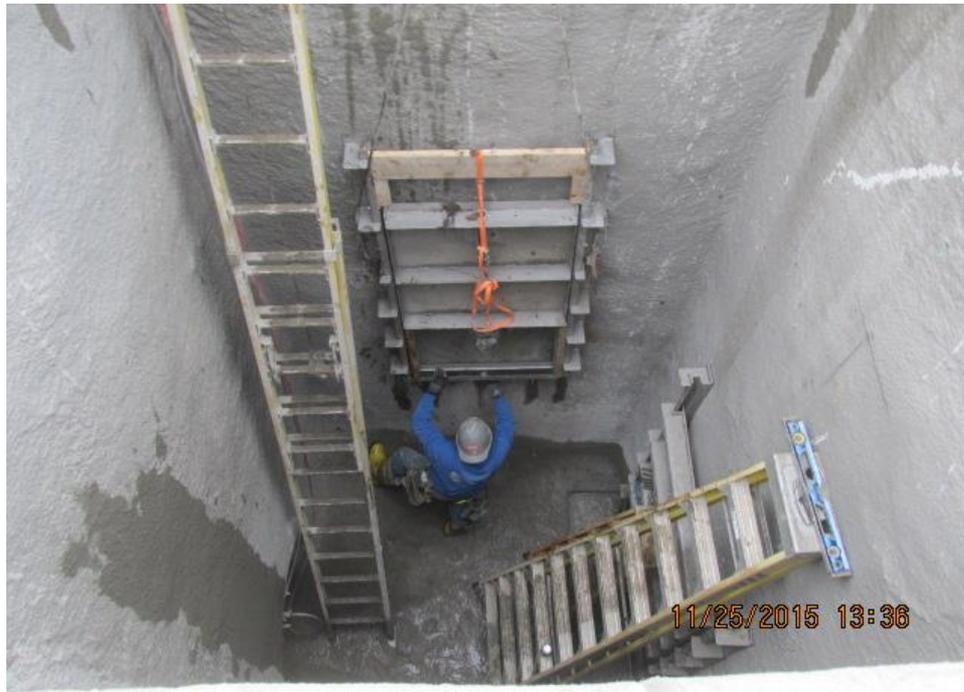



Tuck pointing and brick repair on buildings from the early 1970's













10/13/201



10/14/2015 09:11



Total roof replacement is complete on 3 buildings. Remaining buildings will be done after winter.

