



Lake County Court Expansion Project

April 3, 2018

Law and Judicial Committee Update



May 2015 to Present



**Tunnel
May 2015-
May 2016**

**Court Tower
May 2016-
May 2018**

Construction Update

Jail Kitchen Renovations

Start September 2017 / Finish April 2018

Food preparation performed off site



Construction Update

Babcox Basement

Started November 2017

Underground plumbing work for new Bullpen complete



Robison
Guarnery Inc.

AECOM




Construction Update

Court Tower – 1st Floor Lobby



Construction Update

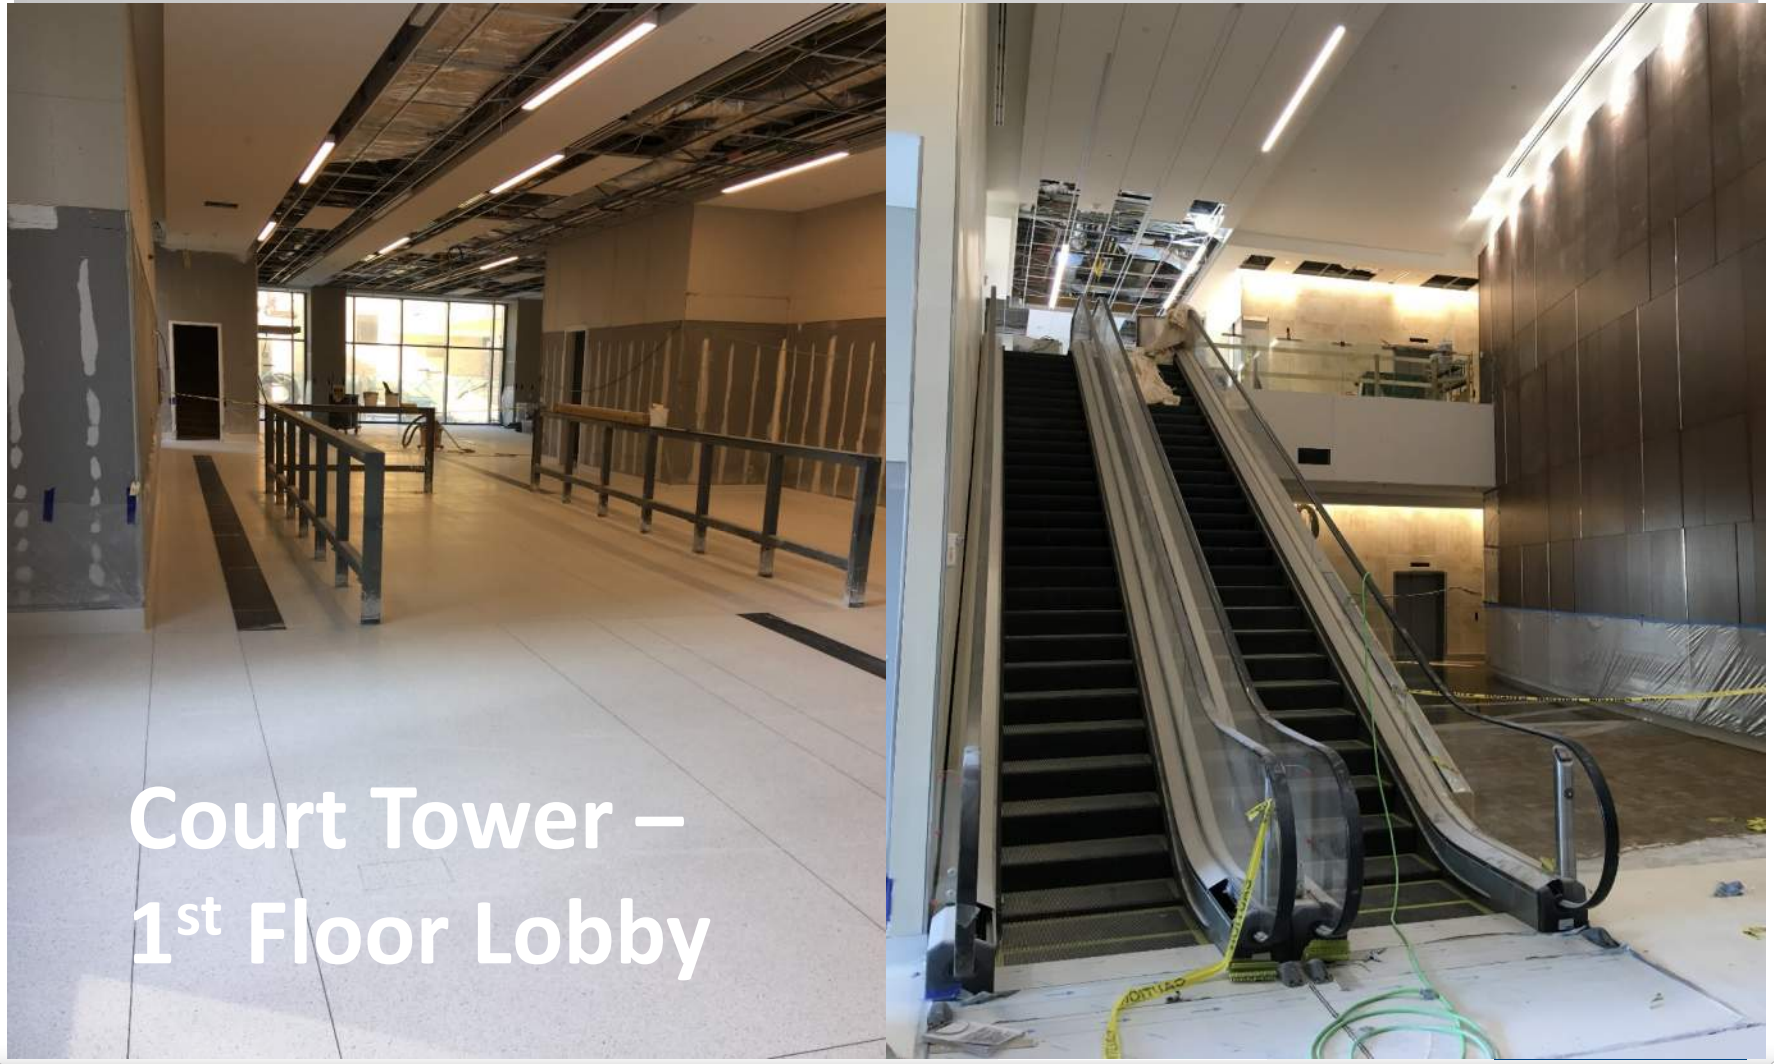

Court Tower –
1st Floor Lobby

Construction Update



Construction Update



The Bridge



Construction Update



Court Tower - Wave

Construction Update



**Court Tower -
Courtroom**



Construction Update

Milestone Dates

- April 2018 – Jail Kitchen Renovations Complete
- May 2018 – Court Tower Substantial Completion
- June 2018 – Court Tower Opening
- June 2019 – Babcox Renovation Opening



Phasing & Transition Plans

- Temporary Bond Court
- Temporary Intake and Booking
- Relocation of Felony Review, Probation Pre-trial & Sheriff personnel
- Relocation Clerk Archival Storage Files


Temporary Bond Court

June 2018 to June 2019

- Simple public access – easy entrance and exiting
- Accommodate building access for weekend calls
- Mitigate impact on other court calls




Robison
Guarnery Inc.

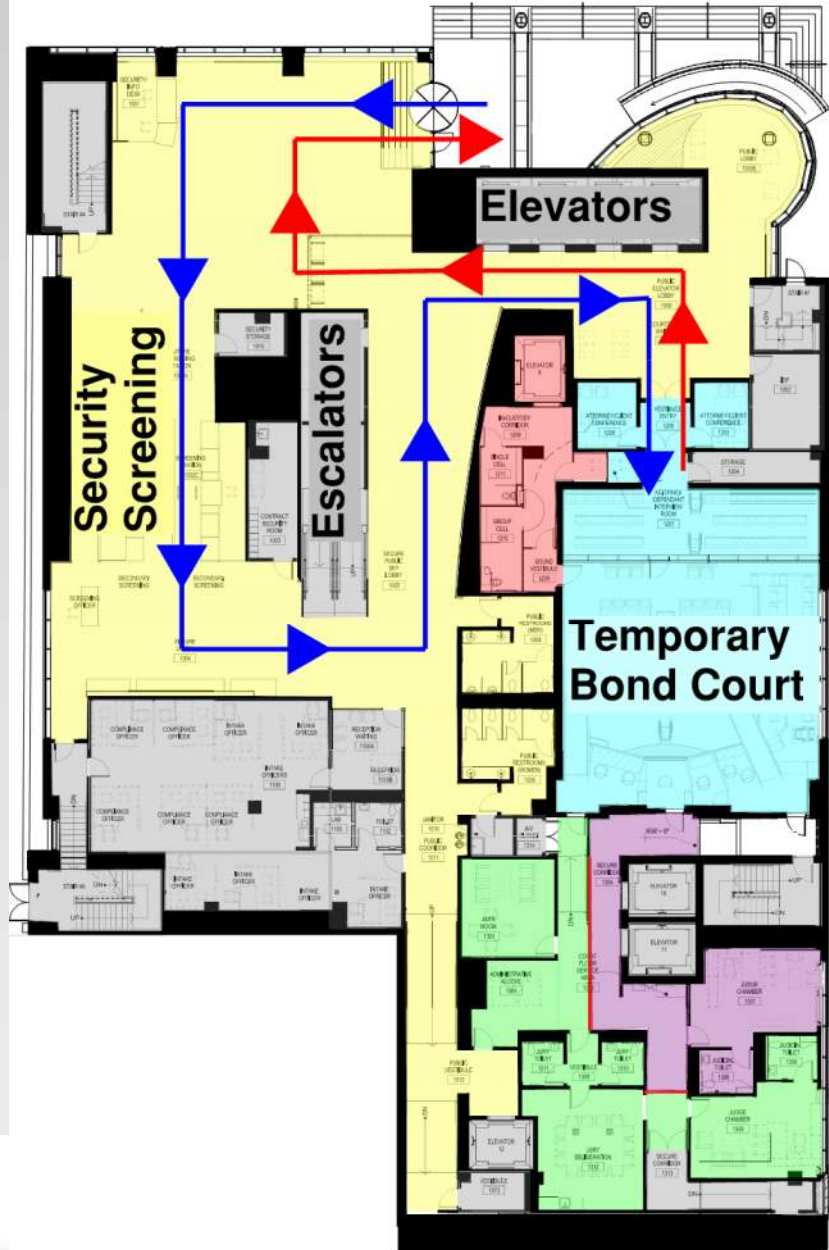


Temporary Bond Court

Felony Review

- Provide temporary office space for 11 staff
- Adjacency/Access to Bond Court critical
- Keep circulation to Bond Court “restricted” access (no public)

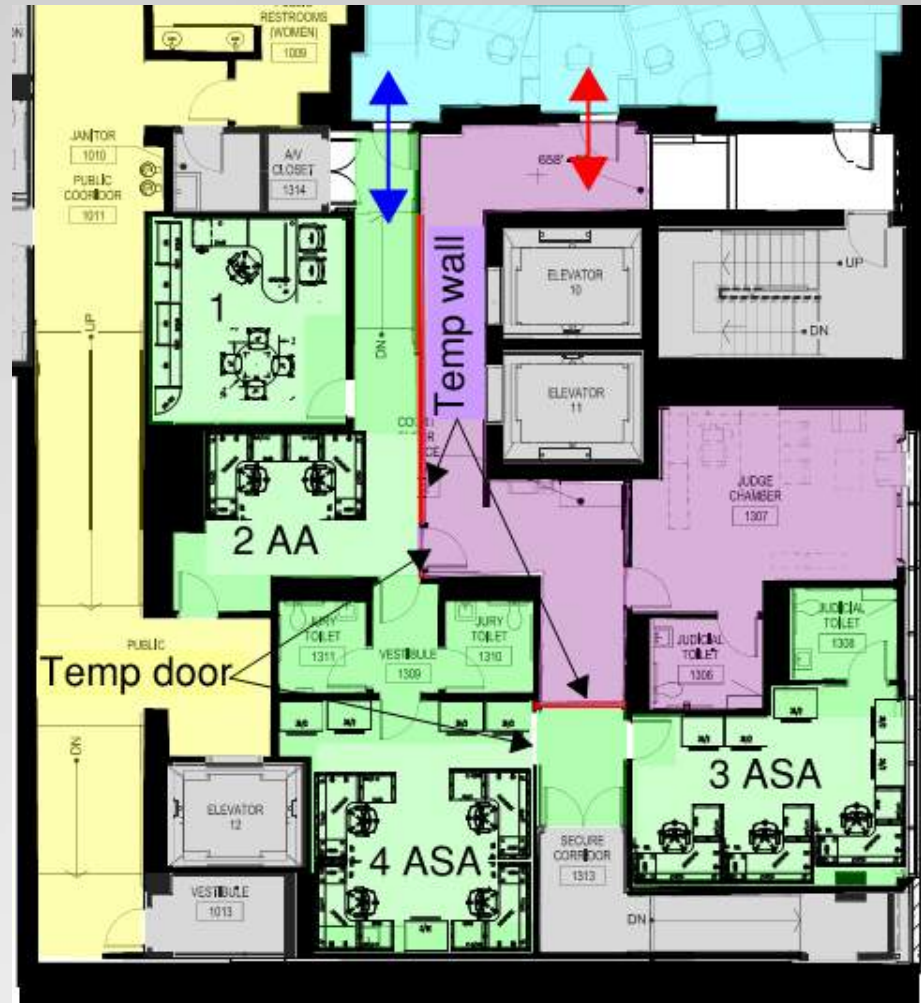


Temporary Intake & Booking

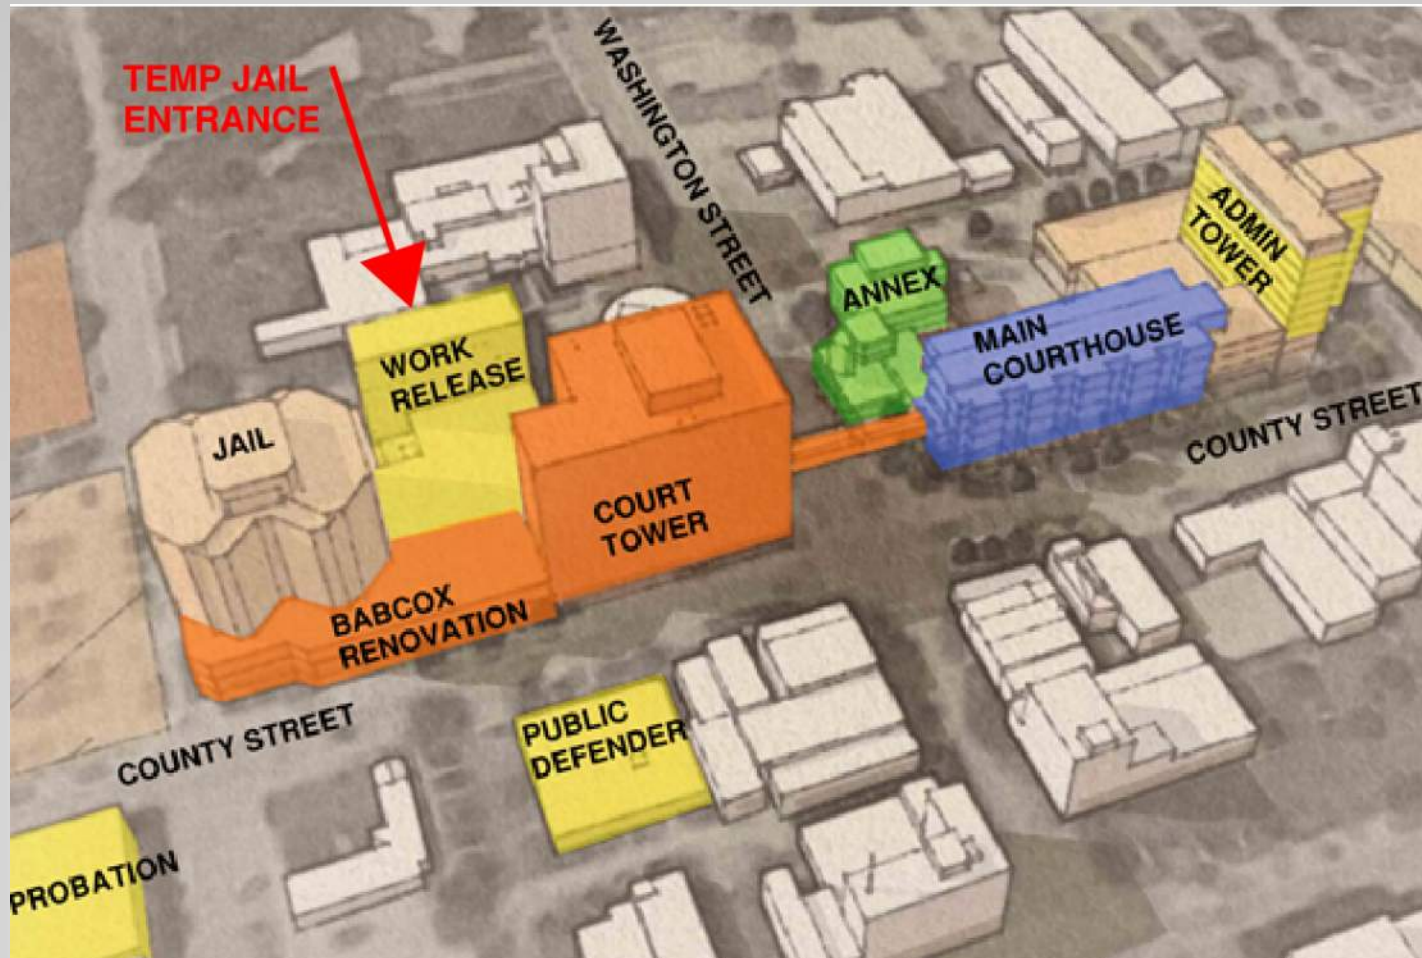

Temporary Intake & Booking

- Public Entrance through CBCC
- New cells in 1-West
- New entrance for intake / pre-book

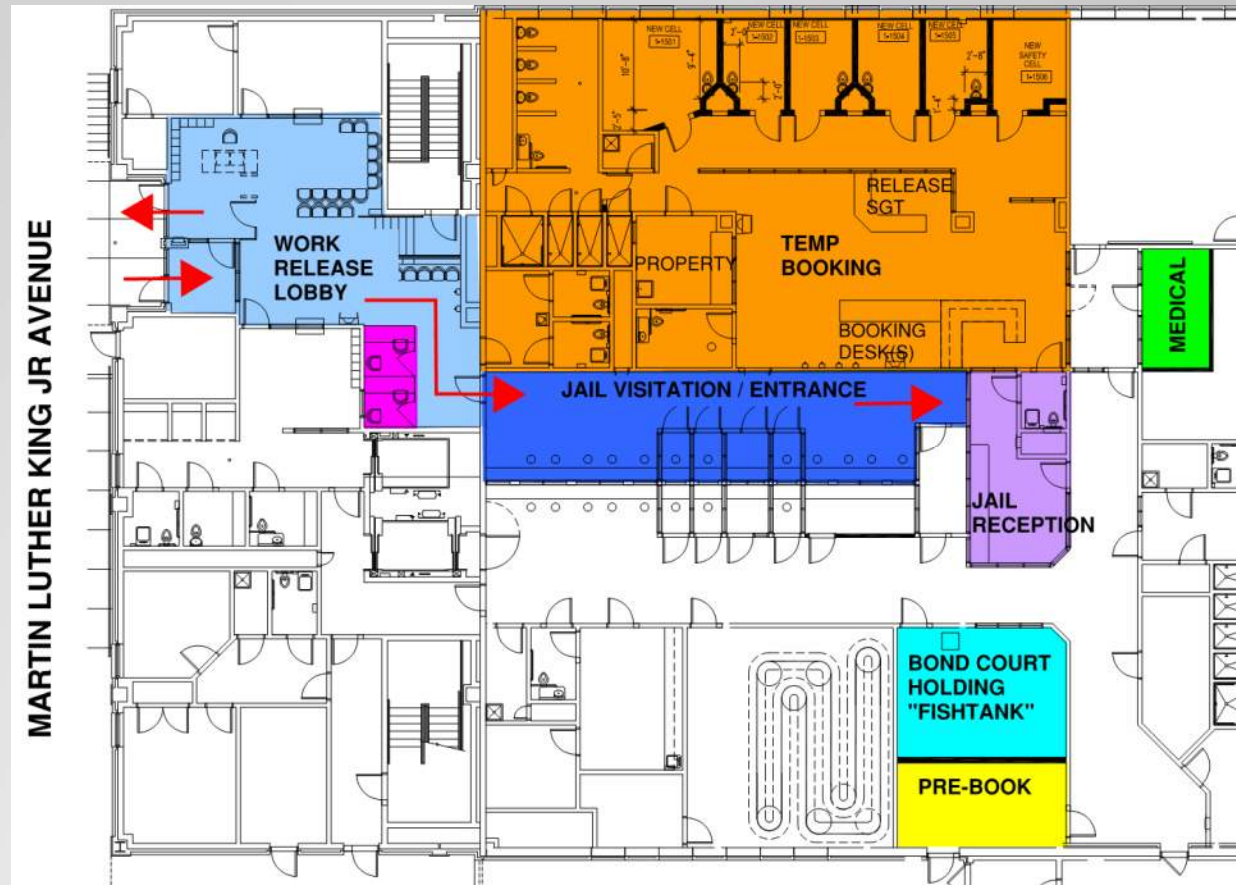

Washington Street Closure

One more time or maybe two.



Robison
Guarnery Inc.

AECOM



Fun Facts

Over 50,000 linear feet of pipe supports used in this scaffolding.

That equates to almost 10 miles of pipe to build this temporary platform.



There are about over 120 workers per day on site.

Fun Facts

Since January 1st, averaged over 110 workers on site per day.



Over 220,000 work hours logged since the steel “topping out” ceremony.



Robison
Guarnery Inc.

AECOM



Thank You



Robison
Guarnery Inc.

AECOM

